

LAB 2 - JIRA HANDS-ON

AGILE BACKLOG CREATION & SPRINT SIMULATIONS

Hyperlocal Courier Dispatch & Tracking Engine

Name: DHAROOR SHIVA SAI VARUN

SRN: PES1UG24CS150

Jira Space: Lab 2 Jira Agile Project (SCRUM)

1. Lab Objective and Required Deliverables

This report documents the Jira implementation of the Lab 2 Agile workflow: converting functional requirements into Epics and User Stories, prioritizing the backlog, assigning Fibonacci-style story points, simulating two sprints, monitoring progress with the Scrum board and Burndown Chart, and reflecting on the sprint outcomes.

Required evidence includes the Jira backlog with Epics/User Stories, story-point assignments, Sprint Board evidence, Burndown Charts, and a reflection addressing estimation, prioritization, sprint alignment, and team capacity.

2. Project Backlog Summary

Epic	Stories	Points
Epic 1 - Delivery Request Management	1	5
Epic 2 - Rider Matching & Dispatch	3	13
Epic 3 - Delivery Verification	2	8
Epic 4 - Multi-Stop Route Optimization	1	8
Epic 5 - Real-Time Tracking & Security	2	16
TOTAL	9	50

3. Story-Point Estimation and Sprint Planning

The final Jira backlog contains 9 User Stories totaling 50 story points. Estimates use the Fibonacci-style values 3, 5, and 8 to represent relative effort, complexity, and uncertainty.

Sprint 1 - 21 points: Create Delivery Request (5), Match Nearest Rider (5), Accept or Reject Dispatch (3), Generate Delivery OTP (3), and Verify Delivery OTP (5).

Sprint 2 - 29 points: Automatically Reassign Rejected Requests (5), Optimize Multi-Stop Route (8), Real-Time Delivery Tracking (8), and Secure OTP and GPS Data (8).

4. Sprint Simulation Process

The board simulation followed the required progression of To Do -> In Progress -> Done. Sprint 1 focused on the core request, matching, dispatch, and OTP workflow. Sprint 2 focused on reassignment, route optimization, tracking, and security. The final Jira evidence shows all 9 planned User Stories in Done status.

5. Evidence Index

1. Backlog - Story Point Assignments
2. Epic 1 - Delivery Request Management
3. Epic 2 - Rider Matching & Dispatch
4. Epic 3 - Delivery Verification
5. Epic 4 - Multi-Stop Route Optimization
6. Epic 5 - Real-Time Tracking & Security
7. Sprint 1 - Board Evidence
8. Sprint 2 - Board Evidence
9. Sprint 1 - Burndown Chart
10. Sprint 2 - Burndown Chart

Image handling: every original screenshot is scaled down proportionally to fit the A4 page. No cropping, stretching, or aspect-ratio distortion is used. The source PNG itself is not edited or recompressed.

Backlog - Story Point Assignments

Jira

Q Search

+ Create

See plans

For you

Recent

Starred

Apps

Plans

Spaces

Filters

Q Search work items

Default filters

My open work items

Reported by me

All work items

Open work items

Done work items

Viewed recently

Created recently

Resolved recently

Updated recently

View all filters

Dashboards

Teams

Goals

Projects

All work items

Q Search all apps

Apps

Share

Ask AI

Basic

JQL

Q Search work

Space

Assignee

Type = Story

Status

More filters


Go back to filter

Save filter

	Work	Priority	Status	Created	Updated	Story point estimate	
☐	SCRUM-22	High	Done	Sep 06, 2026, 10:29 PM	Sep 08, 2026, 7:19 AM	8	
☐	SCRUM-21	High	Done	Sep 06, 2026, 10:28 PM	Sep 07, 2026, 5:16 PM	8	
☐	SCRUM-20	Medium	Done	Sep 06, 2026, 10:26 PM	Sep 07, 2026, 3:41 PM	8	
☐	SCRUM-16	High	Done	Sep 06, 2026, 10:16 PM	Sep 06, 2026, 11:10 PM	5	
☐	SCRUM-15	High	Done	Sep 06, 2026, 10:14 PM	Sep 06, 2026, 11:10 PM	3	
☐	SCRUM-14	High	Done	Sep 02, 2026, 3:04 PM	Sep 07, 2026, 12:14 PM	5	
☐	SCRUM-13	High	Done	Sep 02, 2026, 3:02 PM	Sep 06, 2026, 11:09 PM	3	
☐	SCRUM-12	High	Done	Sep 02, 2026, 2:59 PM	Sep 06, 2026, 11:07 PM	5	
☐	SCRUM-11	High	Done	Sep 02, 2026, 2:55 PM	Sep 06, 2026, 11:07 PM	5	

9 of 9

Epic 1 - Delivery Request Management

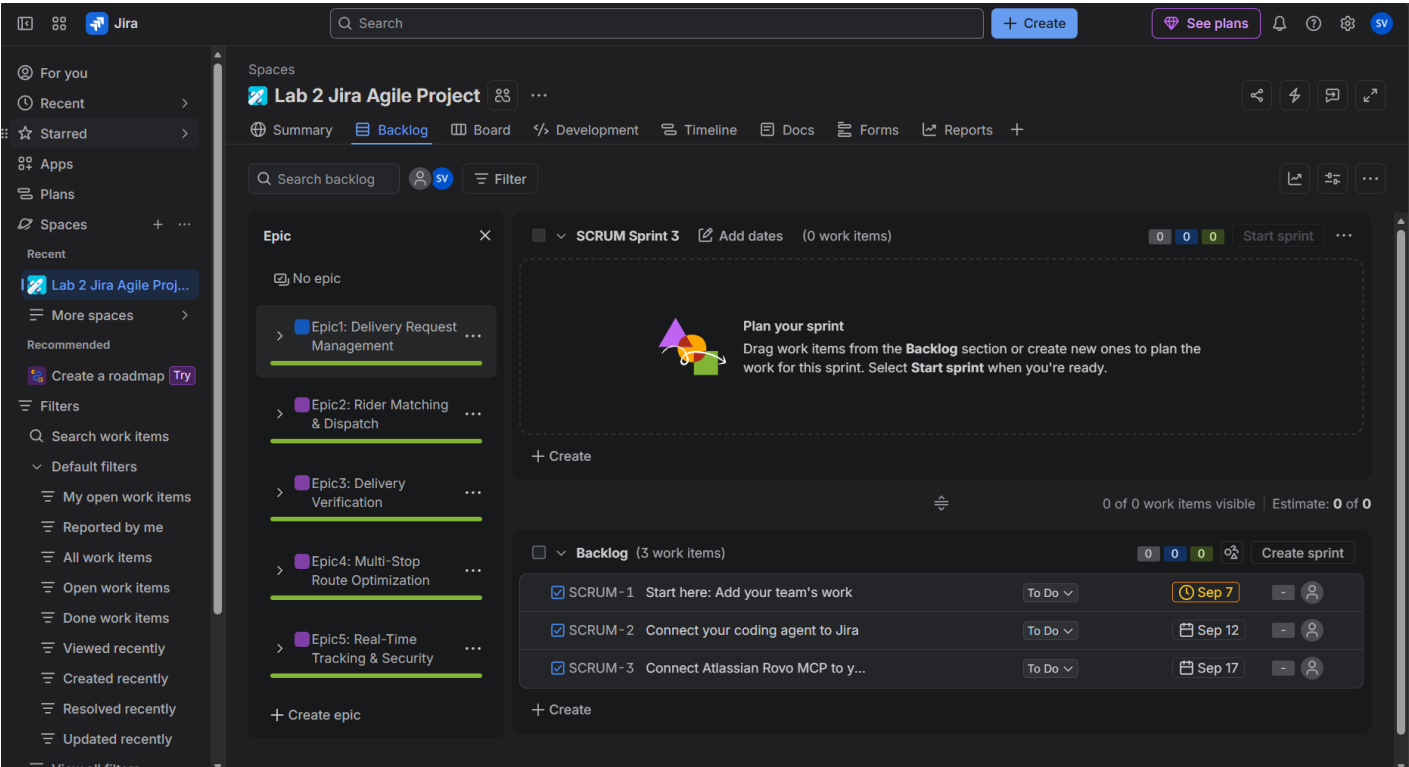

Epic 2 - Rider Matching & Dispatch

For you

Recent

Starred

Apps

Plans

Spaces

Recent

Lab 2 Jira Agile Project

More spaces

Recommended

Create a roadmap

Try

Filters

Dashboards

Teams

Goals

Projects

Customize sidebar

Spaces / Lab 2 Jira Agile Pro... / SCRUM-7

Epic2: Rider Matching & Dispatch

Description

Match delivery requests with nearby active riders and manage dispatch acceptance, rejection, and reassignment.

Attachments

Add attachment

Create project plan

Try

Child work items

100% Done

Work	Pri...	As...	Status
SCRUM-12 Match Nearest Rider	H.	SV s	Done
SCRUM-13 Accept or Reject Dispatch	H.	SV s	Done
SCRUM-14 Automatically Reassign Rejected Requests	H.	SV s	Done

Linked work items

Add linked work item

Create

1

To Do

Improve Epic

Details

Assignee

Unassigned

Assign to me

Labels

Add labels

Sprint

Add sprint

Due date

Add due date

Parent

Add parent

Team

Add team

Start date

Add date

Story point estimate

Add story points

Reporter

SV shiva sai varun

Development

Automation

Rule executions

Created last week

Configure

Epic 3 - Delivery Verification

For you

Recent

Starred

Apps

Plans

Spaces

Recent

Lab 2 Jira Agile Project

More spaces

Recommended

Create a roadmap

Filters

Dashboards

Teams

Goals

Projects

Customize sidebar

Search

Create

1

To Do

Improve Epic

Details

Assignee

Labels

Sprint

Due date

Parent

Team

Start date

Story point estimate

Reporter

Development

Automation

Created last week

Configure

Spaces / Lab 2 Jira Agile Pro... / SCRUM-8

Epic3: Delivery Verification

Description

Generate and validate OTPs to securely confirm successful parcel delivery.

Attachments

Child work items

100% Done


Work	Pri...	As...	Status
SCRUM-15 Generate Delivery OTP	H.	SV	Done
SCRUM-16 Verify Delivery OTP	H.	SV	Done

Linked work items

Add linked work item

Add a comment...

Epic 4 - Multi-Stop Route Optimization

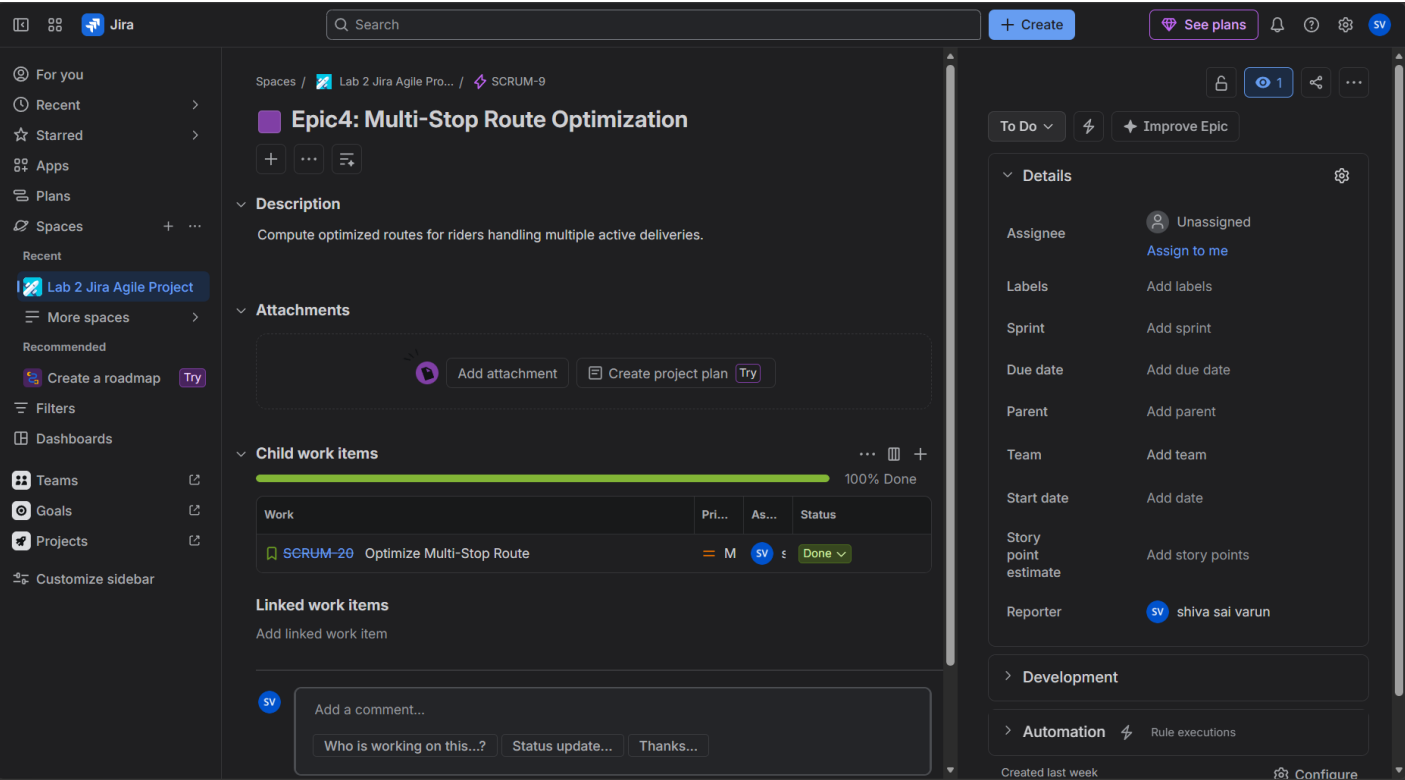

Epic 5 - Real-Time Tracking & Security

For you

Recent

Starred

Apps

Plans

Spaces

Recent

Lab 2 Jira Agile Project

More spaces

Recommended

Create a roadmap

Filters

Dashboards

Teams

Goals

Projects

Customize sidebar

Search

Create

1

To Do

Improve Epic

Details

Assignee

Labels

Sprint

Due date

Parent

Team

Start date

Story point estimate

Reporter

Development

Automation

Created last week

Configure

Spaces / Lab 2 Jira Agile Pro... / SCRUM-10

Epic5: Real-Time Tracking & Security

Description

Provide low-latency delivery tracking while protecting sensitive GPS and OTP data.

Attachments

Child work items

100% Done


Work	Pri...	As...	Status
SCRUM-21 Real-Time Delivery Tracking	H.	SV	Done
SCRUM-22 Secure OTP and GPS Data	H.	SV	Done

Linked work items


Add linked work item

Add a comment...


Sprint 1 - Board Evidence

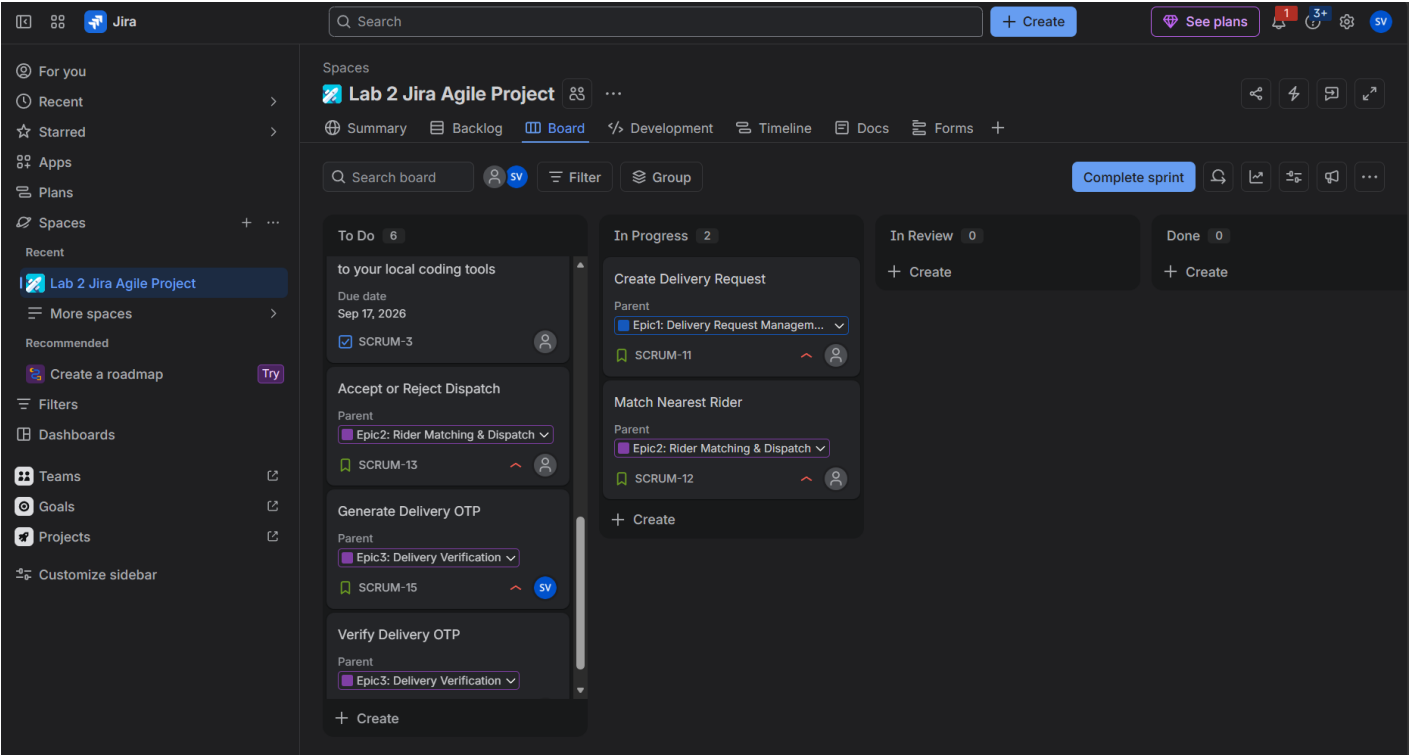

Sprint 2 - Board Evidence

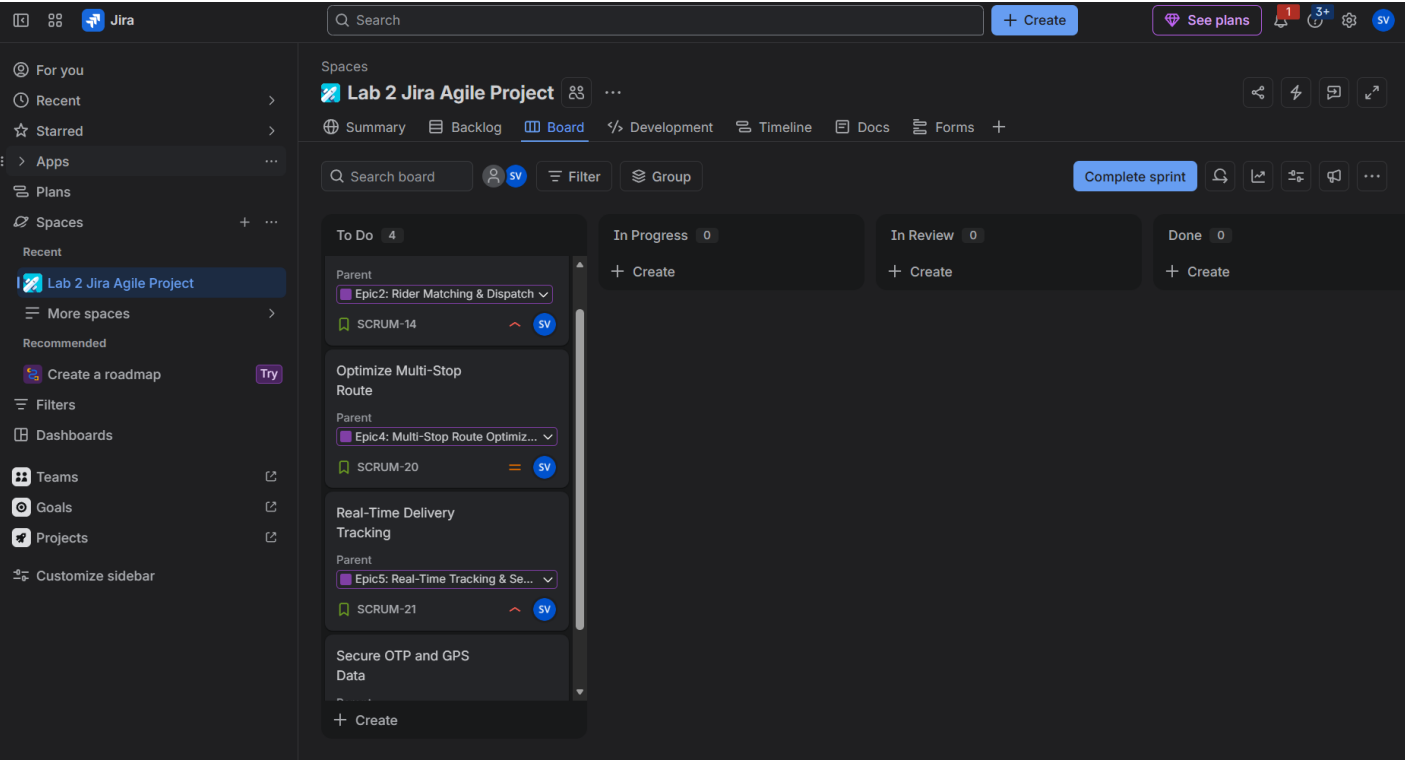

Sprint 1 - Burndown Chart

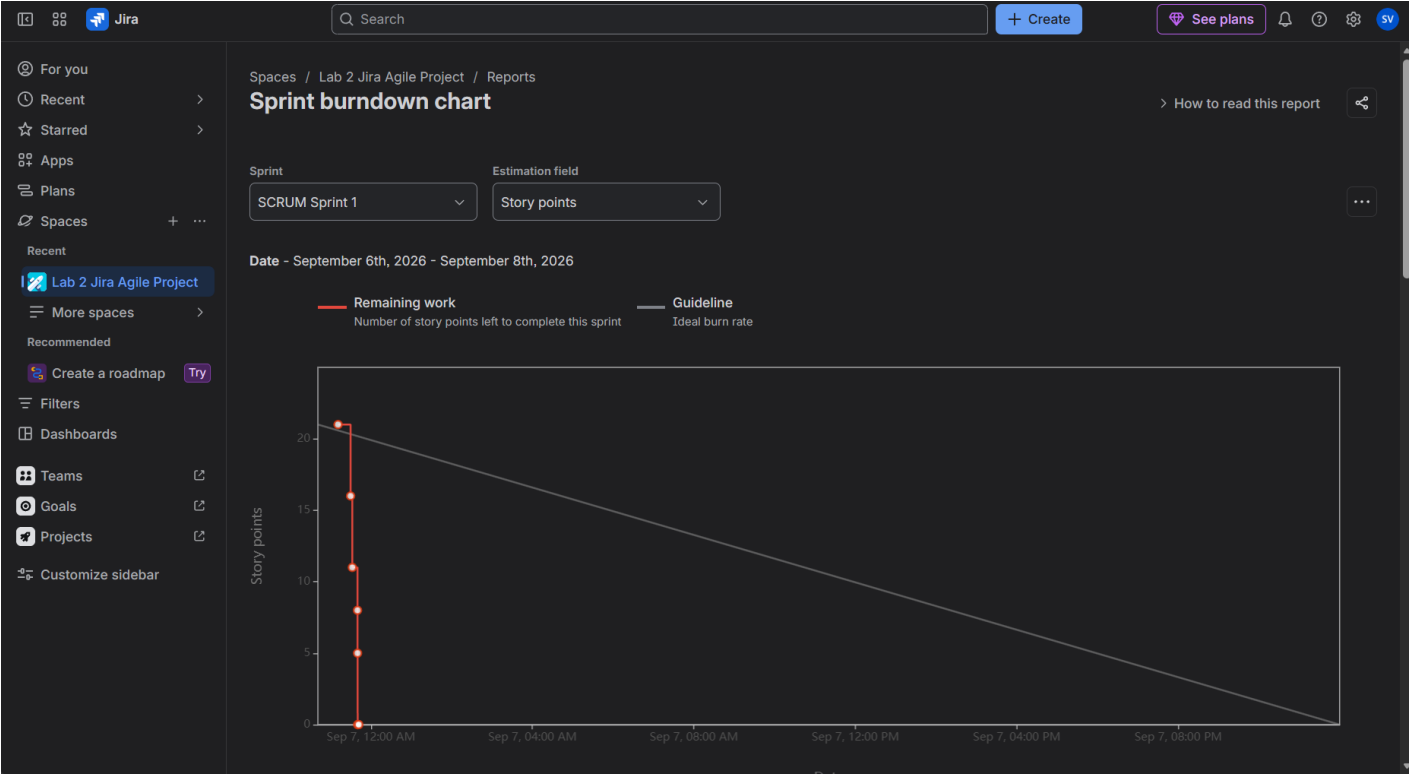

Sprint 2 - Burndown Chart



6. Reflection and Analysis

1. Did your estimations reflect the actual effort?

The estimates generally reflected the relative effort and complexity of the User Stories. Smaller activities such as Generate Delivery OTP and Accept or Reject Dispatch were estimated at 3 points. Core workflow stories were estimated at 5 points, while route optimization, real-time tracking, and security were estimated at 8 points.

2. Was your backlog well-prioritized?

Yes. The backlog prioritized core courier-delivery functionality and operationally important security features. Request creation, rider matching, dispatch response, reassignment, OTP verification, tracking, and security were treated as high-priority work. Multi-stop route optimization was set to medium priority because it improves efficiency after the core delivery flow is established.

3. How did your simulated sprint align with your plan?

The simulation followed the planned Agile flow of To Do -> In Progress -> Done. Sprint 1 focused on delivery request creation, rider matching, dispatch, and OTP verification for 21 points. Sprint 2 covered reassignment, route optimization, real-time tracking, and security for 29 points. The final Jira work-item evidence shows all 9 planned User Stories in Done status.

4. What insights did the burndown chart give about your team's capacity?

Sprint 1's Burndown Chart reached 0 remaining points. Sprint 2's updated Burndown Chart shows the remaining work decreasing from 29 to 24, 16, and 8 story points before reaching 0 by September 8. This indicates that all planned Sprint 2 work was completed and provides a clear view of the team's progress, completion timing, and capacity during the sprint.

7. Conclusion

The Jira exercise demonstrates the Agile lifecycle from requirements decomposition into Epics and User Stories, through prioritization, story-point estimation, Sprint planning, workflow simulation, and Burndown analysis. The completed backlog contains 5 Epics, 9 User Stories, and 50 story points, and the two simulated sprints are documented with original Jira evidence.
